

EXECUTIVE SUMMARY REPORT

St. James Evangelical Lutheran Church

11/22/17

What's New?

Finishes in the building are moving right along. Drywall is finishing up as well as paint. Ceiling grid continues up on 1st floor. Flooring in the lower level has started as well as the kitchen on 1st floor to allow equipment to be installed. The final coat of paint will be installed once casework and flooring is finished.

The Past Week

- Drywall and painting is nearing completion in the addition
- Ceiling grid continues throughout the addition and in the Narthex
- Flooring in the lower level has begun
- Bathroom floor and wall tile
- Casework, countertops, and solid surface sills are installed

Coming Up in the Weeks Ahead


- Complete flooring
- Install ceiling tile after above ceiling inspections are complete
- Bathroom toilet partition installation
- Install doors and hardware



Hallway on 1st floor. Once above ceiling inspection is complete flooring will be installed.



1st floor copy/work room casework is installed.

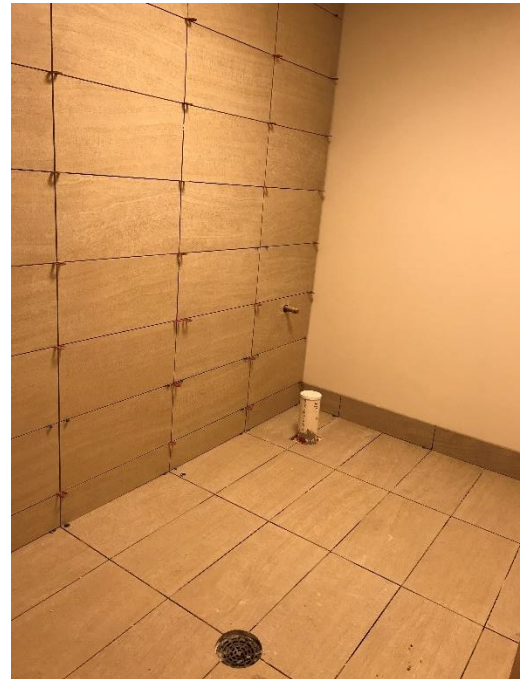

Bathroom floor and wall tile installation in the lower level. Grout to be installed shortly.



Did you know? This past summer, Findorff successfully completed construction projects at 18 schools within 10 different Districts. All this work benefited nearly 10,500 students, and all projects were completed on time!
